

Progress Report on QMH Redevelopment Project

4 July 2019

Paper No. 52/2019


Progress Report

- **Progress of Construction of New Block**
- **Community Communication and Engagement**

Timeline of Construction of New Block

Activity		Date	Remarks
1	Closing of Tender	19 Jan 2018	<ul style="list-style-type: none"> 11 Jan 2018 Consultation with SDC
2	Supported by Panel on Health Services of the Legislative Council	19 Mar 2018	<ul style="list-style-type: none"> 29 Jan 2018 Supplementary information sent to SDC
3	Endorsed by Public Works Sub-Committee of Finance Committee (FC)	25 Apr 2018	
4	Approved by FC of the Legislative Council	18 May 2018	
5	<p>Commencement of Contract</p> <ul style="list-style-type: none"> Demolition works Site formation Superstructure 	<p>31 Oct 2018</p> <p>Mar-Aug 2019 (Tentative) 3Q 2019 (Tentative) 1Q 2021 (Tentative)</p>	<ul style="list-style-type: none"> 5 Jul 2018 Progress report to SDC 8 Nov 2018 Progress report to SDC 7 Mar 2019 Progress report to SDC 4 Jul 2019 Progress report to SDC
6	Completion of Construction of New Block	2024 (Tentative)	

Stacking of New Block (Tentative)

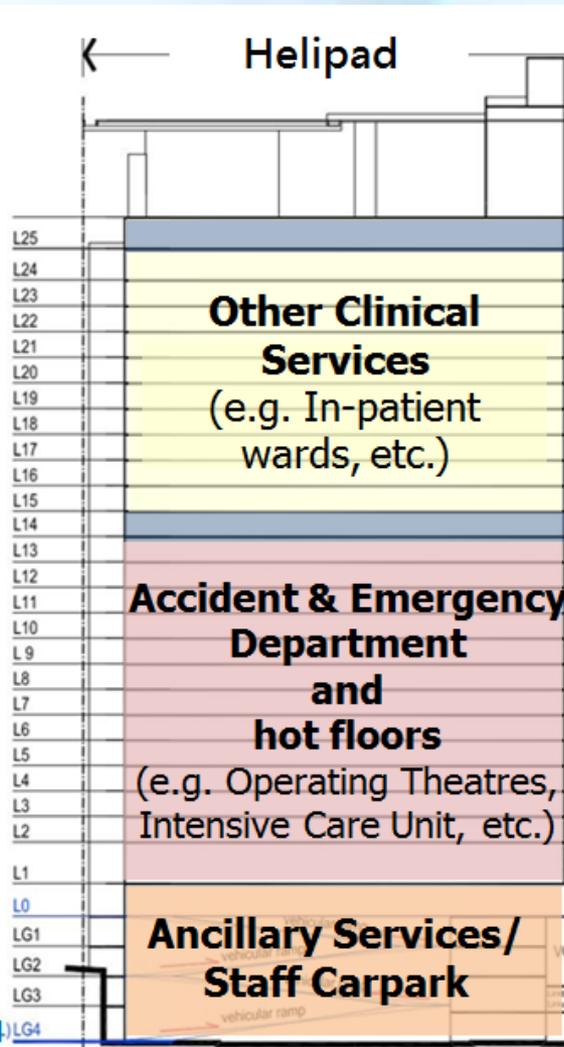

- the New Block will mainly accommodate Accident and Emergency (A&E) Department, Emergency Medicine Wards, Diagnostic Radiology Department, Operating Theatres, Cardiac Catheterization Laboratories, Intensive Care Unit/ Paediatric Intensive Care Unit and In-patient Wards.
- adopt a patient-oriented design with well-coordinated services and convenient connection between the A&E Department and hot floors so as to strengthen emergency services for critical patients
- a rooftop helipad will be for enhancement of transportation arrangement of life saving service

Demolition Works

- Demolition of Pathology Building, Housemen Quarters and the link bridges between Clinical Pathology Building and Block K completed
- Setup of gantries on Pok Fu Lam Road completed
- Demolition of Clinical Pathology Building in progress



Setup of Gantries on Pok Fu Lam Road
(Completed)



Link Bridges between Clinical Pathology Building and Block K
(Demolition completed)



Estimated No. of Construction Site Vehicle

Stage	Estimated No. of Site Vehicles	
	Max. Qty./ Hour	Max. Qty./ Day
Demolition Stage	4	30
Site Formation Stage	6	50



Cleansing of vehicle wheels for dust control



Wheels washing facility
(Sedimentation tank underneath)

Traffic Safety Control Measures



Traffic Warden




CCTV



Traffic Signals at Gantries



Automatic Audio Alert System

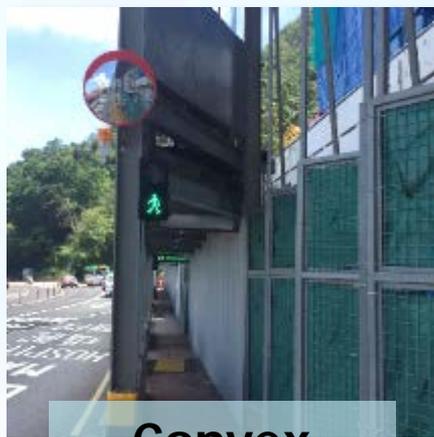

Convex Mirror





Warning Strips at Concrete Plinths



Anti-slipage Metal Plates w/ Warning Strips at Gantries

Re-provisioning of Footpath to Kotewall Road

- To minimize the impact on trees and slope excavation and to achieve shorter construction period, the design of footpath has been modified and agreed by technical departments (relevant information has been submitted to SDC in May)
- Target completion in June 2019. For the subsequent maintenance of the footpath, it is recommended that Home Affairs Department will take up the maintenance of the re-provisioned footpath (excluding any slope maintenance works) according to the arrangement of District Minor Works projects

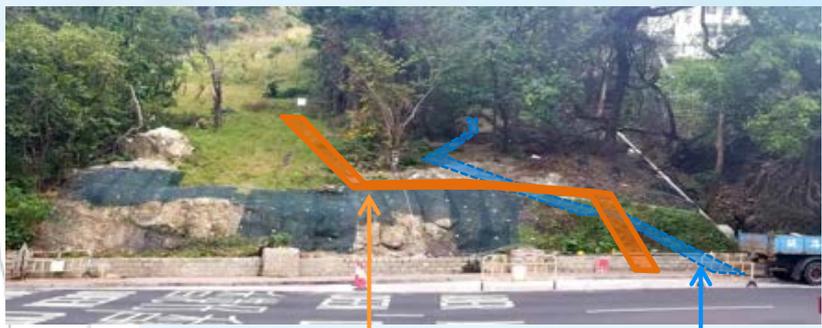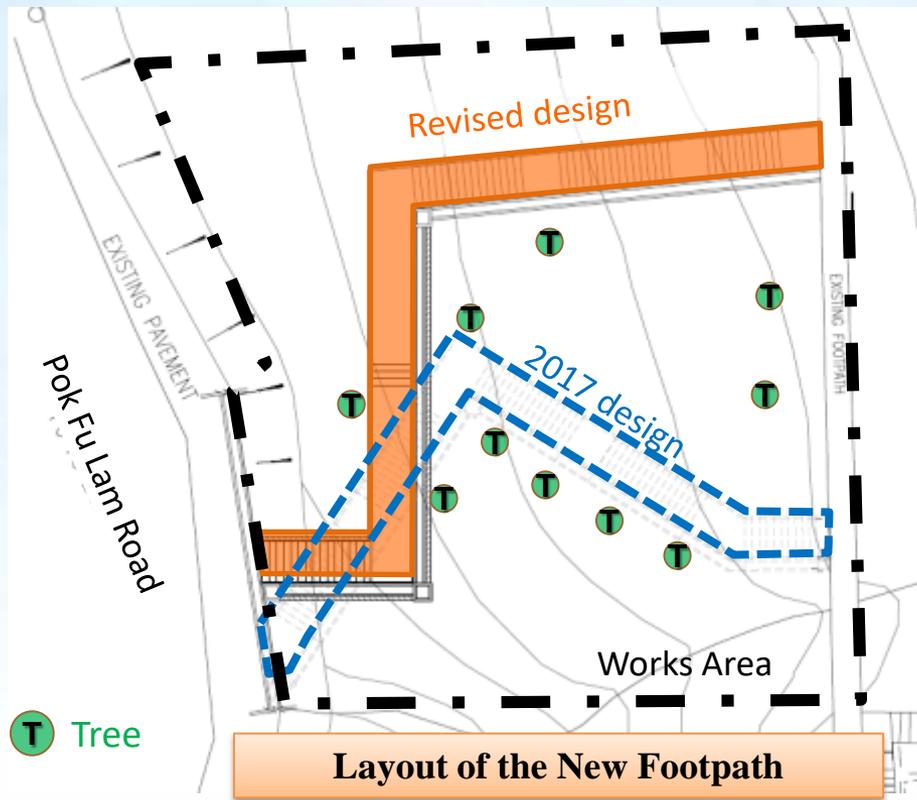

Revised setting out
Previous setting out



The re-provisioned footpath

QMH Redevelopment Community Newsletter (5th issue)

- published and distributed to the community in April 2019



Thank you!
