

Progress Report on QMH Redevelopment Project

5 July 2018 Paper No. 57/2018



Progress Report

- ➤ Stage 1 Senior Staff Quarters (Block T) Conversion Works
- Stage 2 Preparatory Works for Construction of New Block
- Community Communication and Engagement
- Discussion of Improvements to the Existing Lifts and Access to QMH




Update on

Stage 1 Senior Staff Quarters (Block T) Conversion Works

Stage 1 Senior Staff Quarters (Block T) Conversion Works

Redevelopment

The associated relocation works of the Senior Staff Quarters (Block T) Conversion Works are generally on schedule and is expected to be completed in **July 2018**

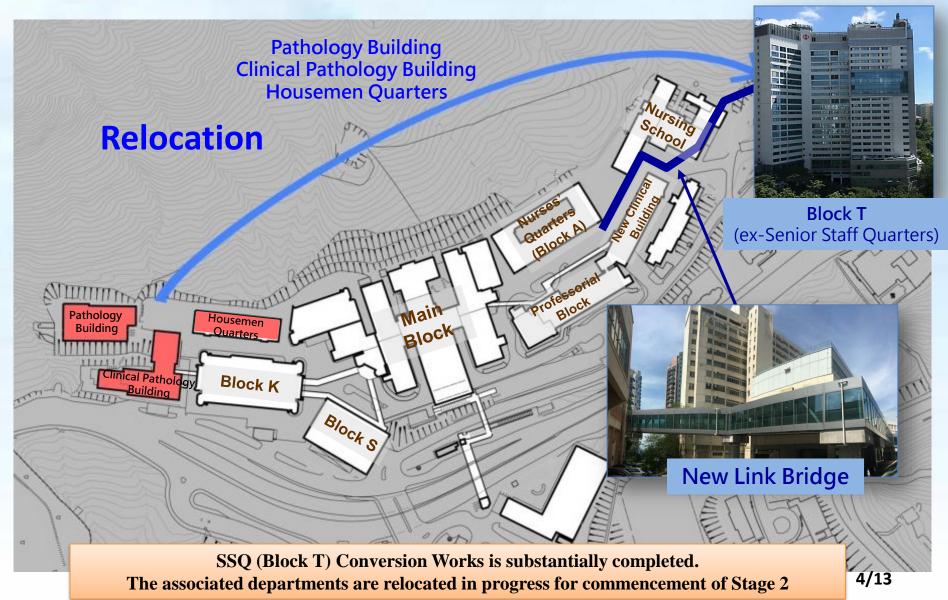

Stage 1 Senior Staff Quarters (Block T) Conversion Works Update

Update on White Powder Incident



Independent Investigation Expert Assessment Report

Major Cause of White Powder: Due to chemical reaction caused by exposure of the aluminum cooling coils of the air handling units (AHUs) to ozone gas generated by the UV lamps installed inside the AHUs

Rectification: To replace all the concerned cooling coils and terminate the use of UV Lamps

Remedial Measures and Status

- Terminate the use of UV Lamps (Completed)
- Replace all the concerned cooling coils (Completed)
- Cleansing of the concerned air ducts (Completed)
- Conduct second round of air sampling tests (Completed, result to be ready in early Jul)
- Regular checking and monitoring of white powder issue (no white powder is found so far after the replacement)

Staff Communication & Support

- Weekly staff briefing session
- Weekly e-flyer
- N95 masks and fit tests
- Staff hotline and WhatsApp group
- Staff clinic special arrangement



Update on

Stage 2 Preparatory Works for Construction of New Block

Stage 2 Preparatory Works for Construction of New Block

Re-provision of Footpath to Kotewall Road

Redevelopment

- The existing slope improvement works by CEDD at the concerned area is still in progress
- Construction works of the footpath will commence in 2 months time after CEDD's handed back the slope to LandSD





Stage 2 Preparatory Works for Construction of New Block



Timeline of Construction of New Block

Item	Activity	Date	Remarks
1	Closing of Tender	19 Jan 2018	 11 Jan 2018 Consultation with SDC 29 Jan 2018 Supplementary information sent to SDC 8 Mar 2018 Progress report to SDC
2	Supported by Panel on Health Services of the Legislative Council	19 Mar 2018	
3	Endorsed by Public Works Sub- Committee of Finance Committee (FC)	25 Apr 2018	
4	Approved by FC of the Legislative Council	18 May 2018	 5 Jul 2018 Progress report to SDC 3Q 2018
5	Commencement of Contract	Oct 2018 (Tentative)	Community Liaison Group will be formed for discussions of related matters and concerns from the community about the QMH Redevelopment Project 8 Nov 2018
6	Completion of Construction of New Block	2024 (Tentative)	Latest updates to be presented in SDC Meeting for comments 8/13

Community Communication & Engagement

- Queen Mary Hospital
- The 1st Community Forum on Redevelopment of QMH in 2018 was successfully held on 7 March 2018 at Aberdeen Kaifong Welfare Association
- The 2nd Community Forum in 2018 is expected to be held in 4Q 2018.
 District council members and public are welcome to join.











Community Communication & Engagement

 the 3rd issue of community newsletter was distributed to the community in May 2018



3rd Issue of QMH Redevelopment Project Community Newsletter

Community Communication & Engagement

Community Liaison Group

- Community Liaison Group will be formed in 3Q 2018
- to provide a direct communication channel with District Council as well as various community stakeholders
- for discussions of related matters and concerns from the community about the QMH Redevelopment Project

Discussion of Improvements to the Existing Lifts and Access to QMH

- Meeting with SDO and FEHD representatives was held on 9 April 2018
- Feedback from the public and patients about the existing facilities and suggestions for improvement were shared in the meeting





Thank you!
