



Progress update on Queen Mary Hospital Redevelopment, Phase 1

Southern District Council Meeting 14 May 2015









- Report on progress update
 - Stage 1 Senior Staff Quarters (SSQ) Conversion Works
 - Stage 2 Preparatory Works for Construction of New Block
 - Internet Website for QMH Redevelopment Project







Progress update

Stage 1 Senior Staff Quarters (SSQ) Conversion Works



1. Senior Staff Quarters (SSQ) Conversion Works

- The SSQ conversion and associated works are generally on schedule.
- The Environmental Protection Department conducted a surprise site inspection on 16 April 2015. No adverse comment was received.








2. Study on Use of Roads and Pavements

- QMH would appoint a consultant to study the pedestrian and vehicular traffic flows within and around QMH.
- Concerns from the SDC and the neighbours would be covered.
- QMH is consolidating professional advice for drafting preliminary concepts for improvements.

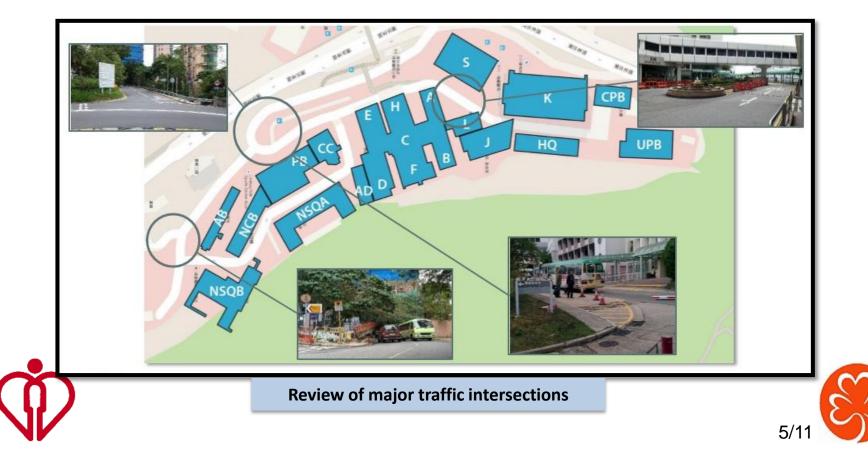






Progress update on

Stage 2 Preparatory Works for Construction of New Block



1. Proposed Rooftop Helipad

- The Environmental Protection Department (EPD) issued the Environmental Impact Assessment (EIA) Study Brief in April 2015.
- The Architectural Services Department (ArchSD) would prepare the Environmental Impact Assessment report based on the Study Brief. The EIA report is expected to be submitted to EPD by 4Q 2015.

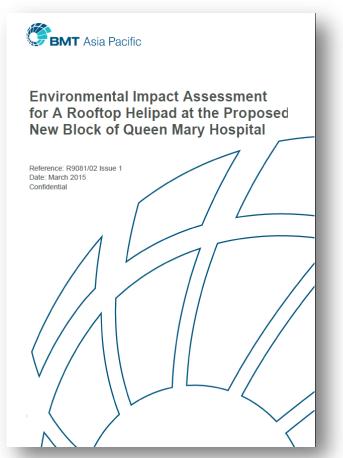






2. Noise Mitigation Measure

- Installation of Double-glazed Windows
 - The installation of double-glazed windows in Blocks J and K was in progress and installation works for 13 wards have been completed.
 - The scope has been extended to cover the Block K elevation facing Pokfulam Road to further reduce the potential noise nuisance.
 - It was targeted to be completed in 1Q 2016.





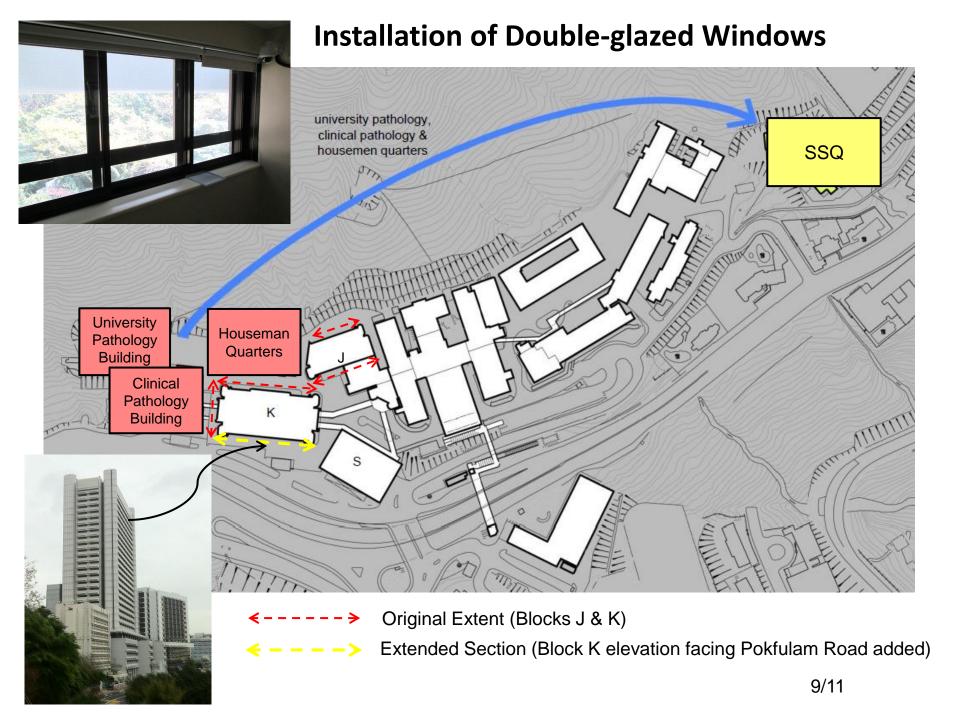





Internet Website for QMH Redevelopment Project



Internet Website for QMH Redevelopment Project

- An internet website would be developed to enhance two-way communication.
- Expected to be launched within 2015/16.





11/1
