

Progress Report on QMH Redevelopment Project

7 March 2019


Paper No. 21/2019

Progress Report

- **Progress of Construction of New Block**
- **Community Communication and Engagement**

Stage 1 Senior Staff Quarters (Block T) Conversion Works

- Last phase of the associated relocation works completed on 3 August 2018 for commencement of Stage 2 - Construction of New Block

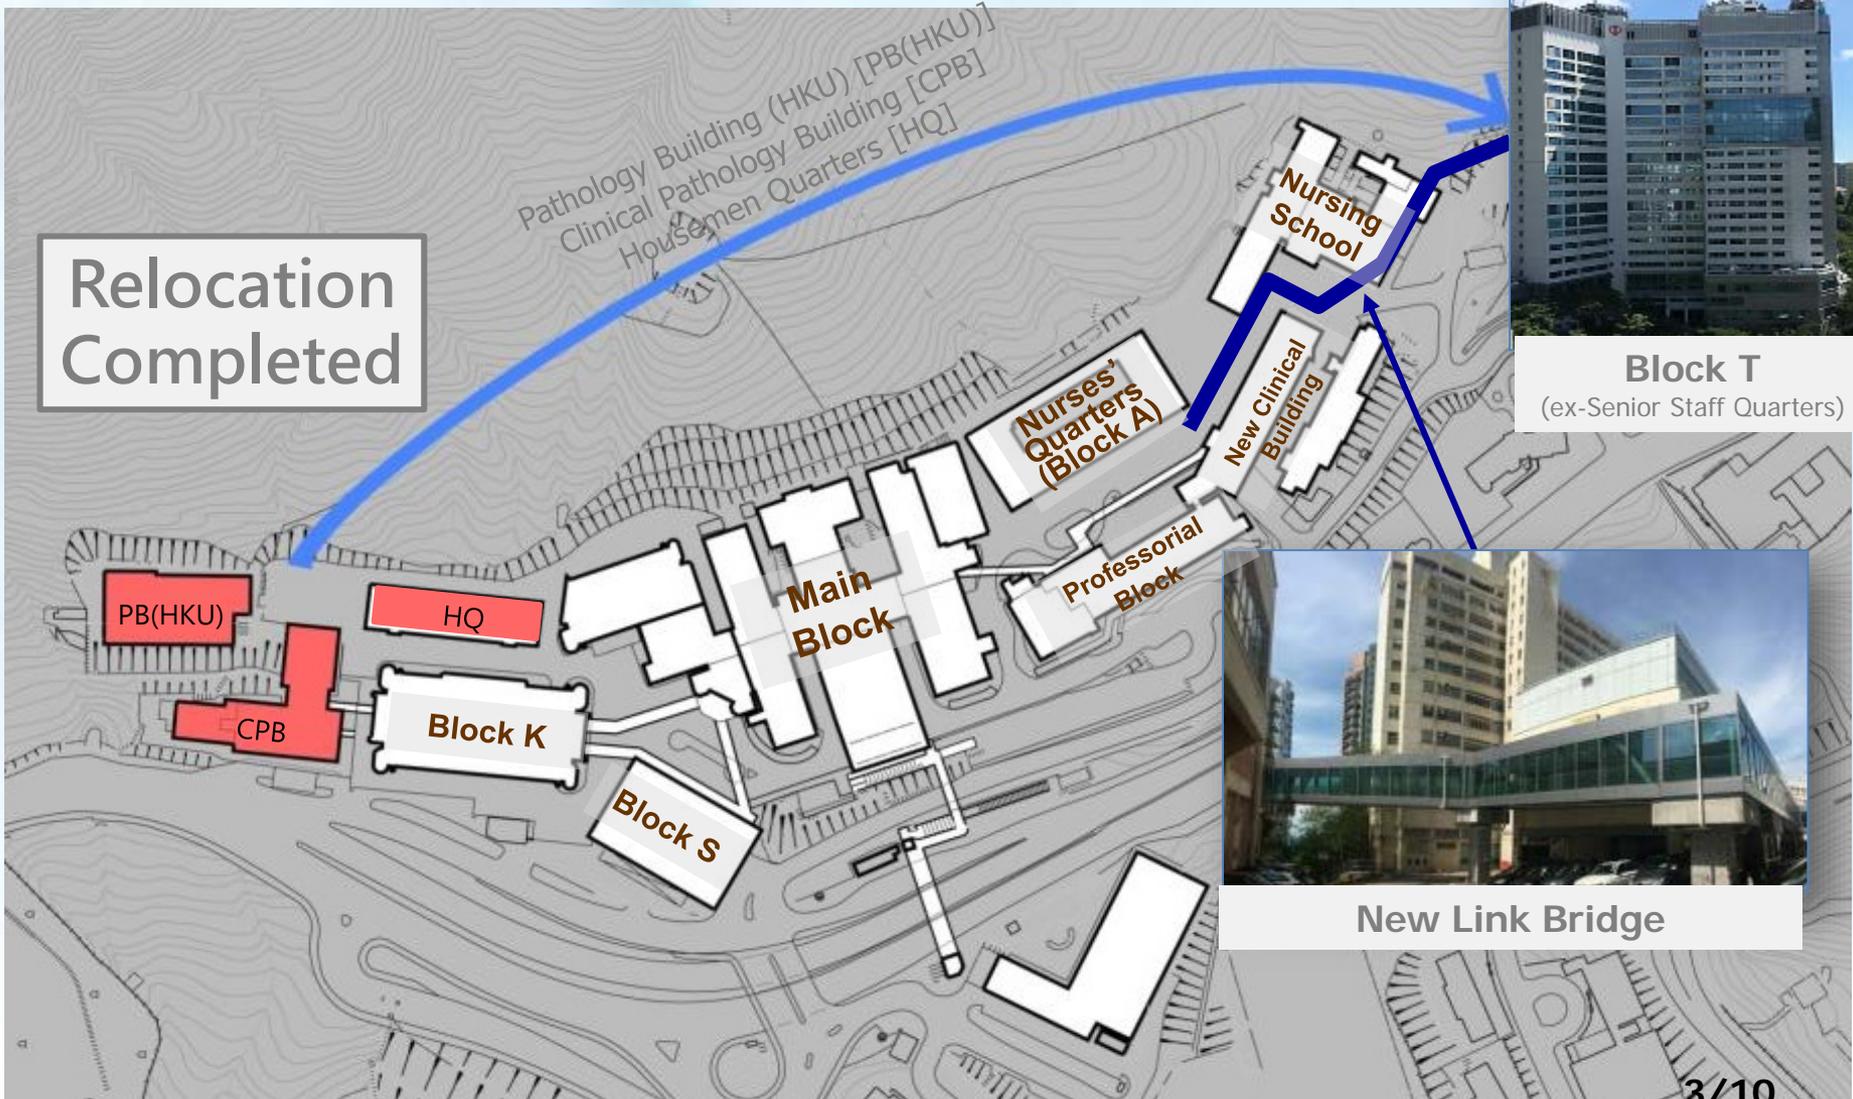

Relocation Completed




Block T
(ex-Senior Staff Quarters)



New Link Bridge

Stage 2 Construction of New Block

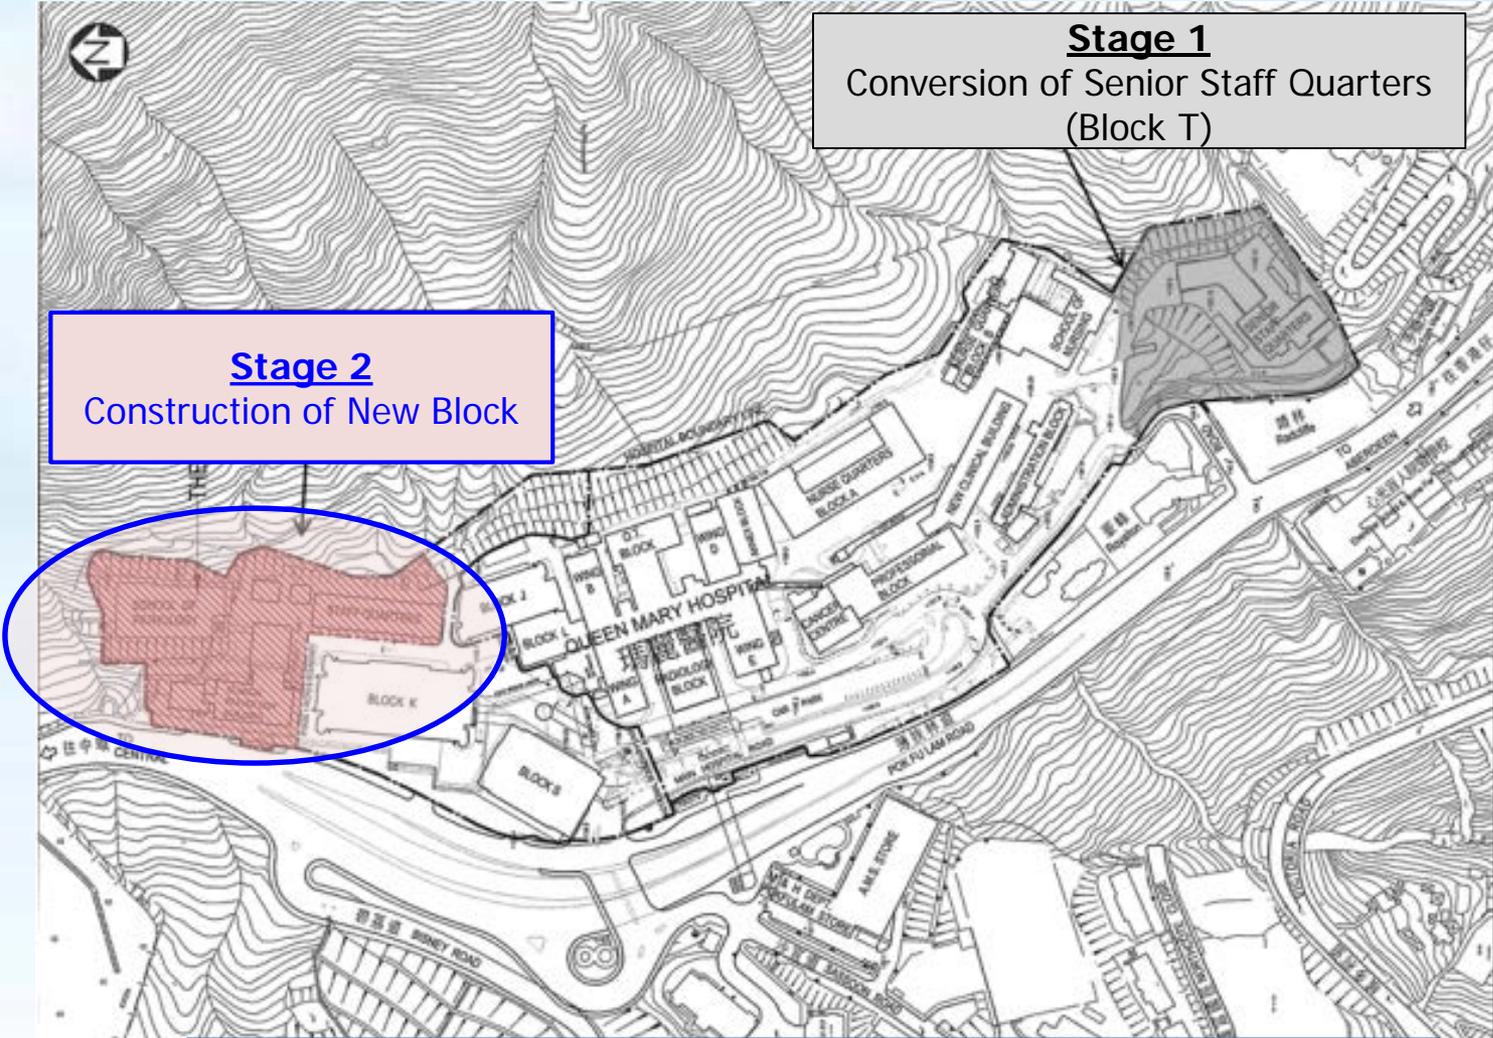

Stage 1
Conversion of Senior Staff Quarters
(Block T)

Stage 2
Construction of New Block

Demolition of Clinical Pathology Building, Pathology Building (HKU) and Housemen Quarters for Construction of New Block

Timeline of Construction of New Block

Activity		Date	Remarks
1	Closing of Tender	19 Jan 2018	<ul style="list-style-type: none"> 11 Jan 2018 Consultation with SDC
2	Supported by Panel on Health Services of the Legislative Council	19 Mar 2018	<ul style="list-style-type: none"> 29 Jan 2018 Supplementary information sent to SDC
3	Endorsed by Public Works Sub-Committee of Finance Committee (FC)	25 Apr 2018	<ul style="list-style-type: none"> 8 Mar 2018 Progress report to SDC
4	Approved by FC of the Legislative Council	18 May 2018	<ul style="list-style-type: none"> 5 Jul 2018 Progress report to SDC
5	Commencement of Contract <ul style="list-style-type: none"> Demolition works Site formation Superstructure 	31 Oct 2018 <ul style="list-style-type: none"> Mar 2019 3Q 2019 1Q 2021 	<ul style="list-style-type: none"> 8 Nov 2018 Progress report to SDC
6	Completion of Construction of New Block	2024 (Tentative)	<ul style="list-style-type: none"> 7 Mar 2019 Progress report to SDC

Preparation for Demolition Works

- Site Clearance



- Tree Pruning



- Temporary Traffic Arrangement



Environmental Mitigation Measures



- Provision of noise and dust barriers, atomized spray devices



- Provision of real-time vibration monitoring system



- Regular anti-mosquito measures



- Regular monitoring of air quality and noise level

Re-provisioning of footpath to Kotewall Road

- Commenced in Jan 2019
- Target completion: 2Q 2019

(1) “Living Medical Heritage in the Community” Carnival

(organized by Hong Kong Museum of Medical Sciences)

- Held on 2-3 Mar 2019 at Hong Kong Museum of Medical Sciences & Caine Lane Garden
- Design concept and latest progress of QMH and Grantham Hospital Redevelopment Project will be introduced to the participants through display panels and game booth



(2) QMH Redevelopment Community Newsletter (5th issue)

- to be published and distributed to the community in April 2019

Thank you!
